ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	**1 Pembuatan Sistem Game Challenge**	**73 days?**	**Thu 3/25/21**	**Sat 7/3/21**		
2	**1.1 Observasi dan Pengumpulan Data**	**6 days**	**Thu 3/25/21**	**Thu 4/1/21**		
3	1.1.1 Observasi	3 days	Thu 3/25/21	Mon 3/29/21		Kepala Project
4	1.1.2 Pengumpulan Data	3 days	Tue 3/30/21	Thu 4/1/21	3	Kepala Project
5	**1.2 Perekrutan Anggota Team**	**2 days**	**Fri 4/2/21**	**Mon 4/5/21**	2	Kepala Project
6	**1.3 Perancangan Database dan UML**	**6 days**	**Tue 4/6/21**	**Tue 4/13/21**	**5**	**Database Manage**
7	1.3.1 Perancangan Database	3 days	Tue 4/6/21	Thu 4/8/21	5	**Database Manage**
8	1.3.2 Perancangan UML	3 days	Fri 4/9/21	Tue 4/13/21	7	**Database Manage**
9	**1.4 Perancangan Desain User Interface**	**15 days**	**Wed 4/14/21**	**Tue 5/4/21**	**6**	**UI/UX Designer,K**
10	1.4.1 Perancangan Halaman Login	1 day	Wed 4/14/21	Wed 4/14/21	6	UI/UX Designer
11	1.4.2 Perancangan Halaman Utama	1 day	Thu 4/15/21	Thu 4/15/21	10	UI/UX Designer
12	1.4.3 Perancangan Halaman Dashboard Pelanggan	1 day	Fri 4/16/21	Fri 4/16/21	11	UI/UX Designer
13	1.4.4 Perancangan Halaman Challenge Pelanggan	1 day	Mon 4/19/21	Mon 4/19/21	12	UI/UX Designer
14	1.4.5 Perancangan Halaman Input Challenge Pelanggan	1 day	Tue 4/20/21	Tue 4/20/21	13	UI/UX Designer
15	1.4.6 Perancangan Halaman Riwayat Challenge Pelanggan	1 day	Wed 4/21/21	Wed 4/21/21	14	UI/UX Designer
16	1.4.7 Perancangan Halaman Dashboard Game Master	1 day	Thu 4/22/21	Thu 4/22/21	15	UI/UX Designer
17	1.4.8 Perancangan Halaman Manajemen User Pelanggan Game Master	1 day	Fri 4/23/21	Fri 4/23/21	16	UI/UX Designer
18	1.4.9 Perancangan Halaman Verifikasi Challenge Game Master	1 day	Mon 4/26/21	Mon 4/26/21	17	UI/UX Designer
19	1.4.10 Perancangan Halaman Ranking Challenge Game Master	1 day	Tue 4/27/21	Tue 4/27/21	18	UI/UX Designer

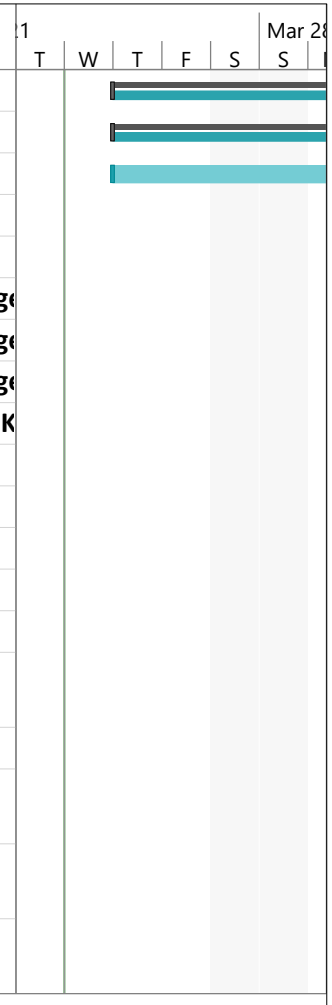

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
20	1.4.11 Perancangan Halaman Manajemen Challenge Game Master	1 day	Wed 4/28/21	Wed 4/28/21	19	UI/UX Designer
21	1.4.12 Review (Meeting Client)	1 day	Thu 4/29/21	Thu 4/29/21	20	UI/UX Designer,Sy
22	1.4.13 Revisi	3 days	Fri 4/30/21	Tue 5/4/21	21	UI/UX Designer,K
23	**1.5 Implementasi Coding & Desain Rancangan Sistem**	**36 days**	**Wed 5/5/21**	**Wed 6/23/21**	**19**	**Kepala Project,Da**
24	**1.5.1 Implementasi Coding**	**22 days**	**Wed 5/5/21**	**Thu 6/3/21**	**9**	**Database Manage**
25	1.5.1.1 Implementasi Coding Halaman Login	2 days	Wed 5/5/21	Thu 5/6/21	22	Database Manage
26	1.5.1.2 Implementasi Coding Halaman Utama	2 days	Fri 5/7/21	Mon 5/10/21	25	Database Manage
27	1.5.1.3 Implementasi Coding Halaman Dashboard Pelanggan	2 days	Tue 5/11/21	Wed 5/12/21	26	Database Management,Pro
28	1.5.1.4 Implementasi Coding Halaman Challenge Pelanggan	2 days	Thu 5/13/21	Fri 5/14/21	27	Database Management,Pro
29	1.5.1.5 Implementasi Coding Halaman Input Challenge Pelanggan	2 days	Mon 5/17/21	Tue 5/18/21	28	Database Management,Pro
30	1.5.1.6 Implementasi Coding Halaman Riwayat Challenge Pelanggan	2 days	Wed 5/19/21	Thu 5/20/21	29	Database Management,Pro
31	1.5.1.7 Implementasi Coding Halaman Dashboard Game Master	2 days	Fri 5/21/21	Mon 5/24/21	30	Database Management,Pro
32	1.5.1.8 Implementasi Coding Halaman Manajemen User Pelanggan Game Master	2 days	Tue 5/25/21	Wed 5/26/21	31	Database Management,Pro
33	1.5.1.9 Implementasi Coding Halaman Verifikasi Challenge Game Master	2 days	Thu 5/27/21	Fri 5/28/21	32	Database Management,Pro
34	1.5.1.10 Implementasi Coding Halaman Ranking Challenge Game Master	2 days	Mon 5/31/21	Tue 6/1/21	33	Database Management,Pro



ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
35	1.5.1.11 Implementasi Coding Halaman Manajemen Challenge Game Master	2 days	Wed 6/2/21	Thu 6/3/21	34	Database Management,Pro
36	**1.5.2 Implementasi Desain**	**36 days**	**Tue 4/20/21**	**Tue 6/8/21**		**Programmer,UI/U**
37	1.5.2.1 Implementasi Desain Halaman Login	3 days	Fri 5/7/21	Tue 5/11/21	25	Programmer,UI/U
38	1.5.2.2 Implementasi Desain Halaman Utama	3 days	Tue 5/11/21	Thu 5/13/21	26	Programmer,UI/U
39	1.5.2.3 Implementasi Desain Halaman Dashboard Pelanggan	3 days	Thu 5/13/21	Mon 5/17/21	27	Programmer,UI/U Designer
40	1.5.2.4 Implementasi Desain Halaman Challenge Pelanggan	3 days	Mon 5/17/21	Wed 5/19/21	28	Programmer,UI/U Designer
41	1.5.2.5 Implementasi Desain Halaman Input Challenge Pelanggan	3 days	Wed 5/19/21	Fri 5/21/21	29	Programmer,UI/U Designer
42	1.5.2.6 Implementasi Desain Halaman Riwayat Challenge Pelanggan	3 days	Fri 5/21/21	Tue 5/25/21	30	Programmer,UI/U Designer
43	1.5.2.7 Implementasi Desain Halaman Dashboard Game Master	3 days	Tue 5/25/21	Thu 5/27/21	31	Programmer,UI/U Designer
44	1.5.2.8 Implementasi Desain Halaman Manajemen User Pelanggan Game Master	3 days	Thu 5/27/21	Mon 5/31/21	32	Programmer,UI/U Designer
45	1.5.2.9 Implementasi Desain Halaman Verifikasi Challenge Game Master	3 days	Mon 5/31/21	Wed 6/2/21	33	Programmer,UI/U Designer
46	1.5.2.10 Implementasi Desain Halaman Ranking Challenge Game Master	3 days	Wed 6/2/21	Fri 6/4/21	34	Programmer,UI/U Designer
47	1.5.2.11 Implementasi Desain Halaman Manajemen Challenge Game Master	3 days	Fri 6/4/21	Tue 6/8/21	35	Programmer,UI/U Designer
48	**1.5.3 Review (Meeting Client)**	1 day	Wed 6/9/21	Wed 6/9/21	47	Database Manage



ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
49	**1.5.4 Revisi**	10 days	Thu 6/10/21	Wed 6/23/21	48	Database Manage
50	**1.6 Pengujian Sistem**	**7 days**	**Thu 6/24/21**	**Fri 7/2/21**	**23**	**Database Manage**
51	1.6.1 Pengujian Sistem Lokal dan Server	2 days	Thu 6/24/21	Fri 6/25/21	49	Database Manage
52	1.6.2 Pengkoreksian dan Revisi Sistem	4 days	Mon 6/28/21	Thu 7/1/21	51	Database Manage
53	1.6.3 Uji Coba Keseluruhan (Final)	1 day	Fri 7/2/21	Fri 7/2/21	52	Database Manage

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21



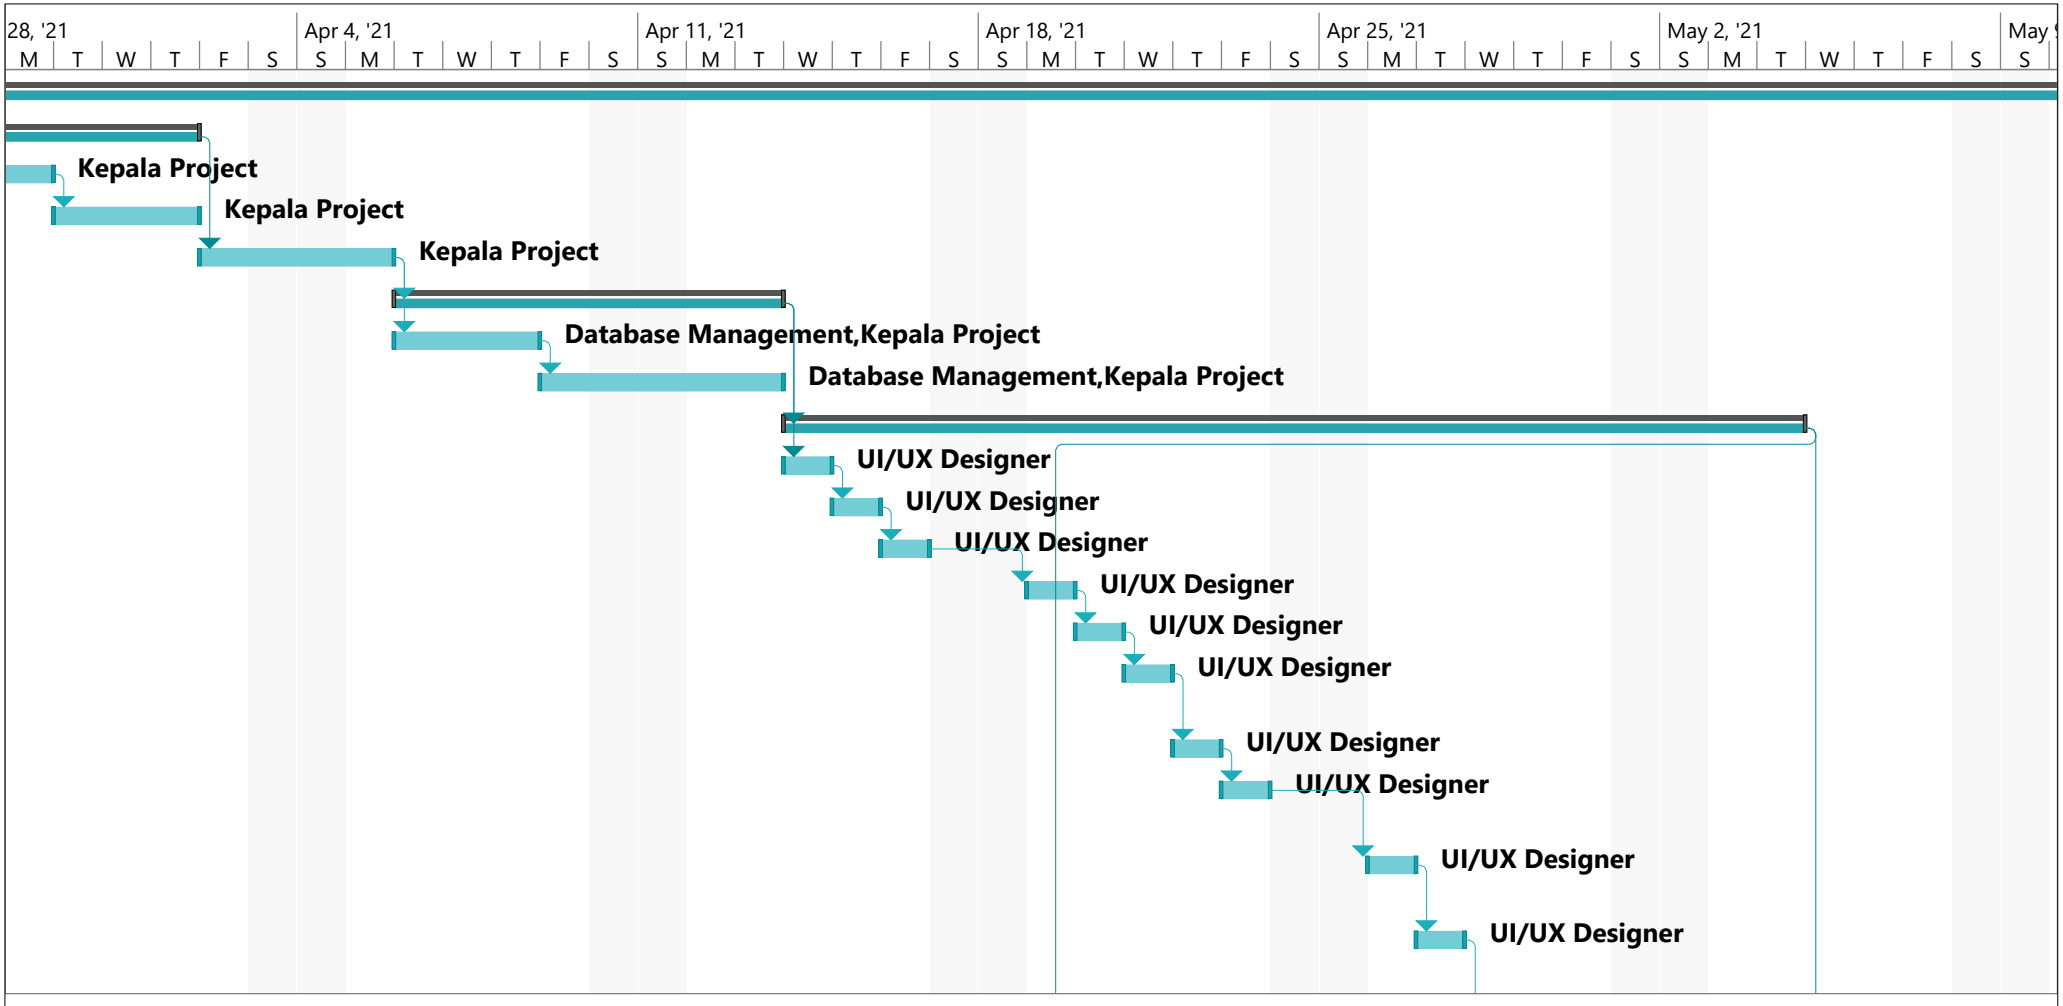

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

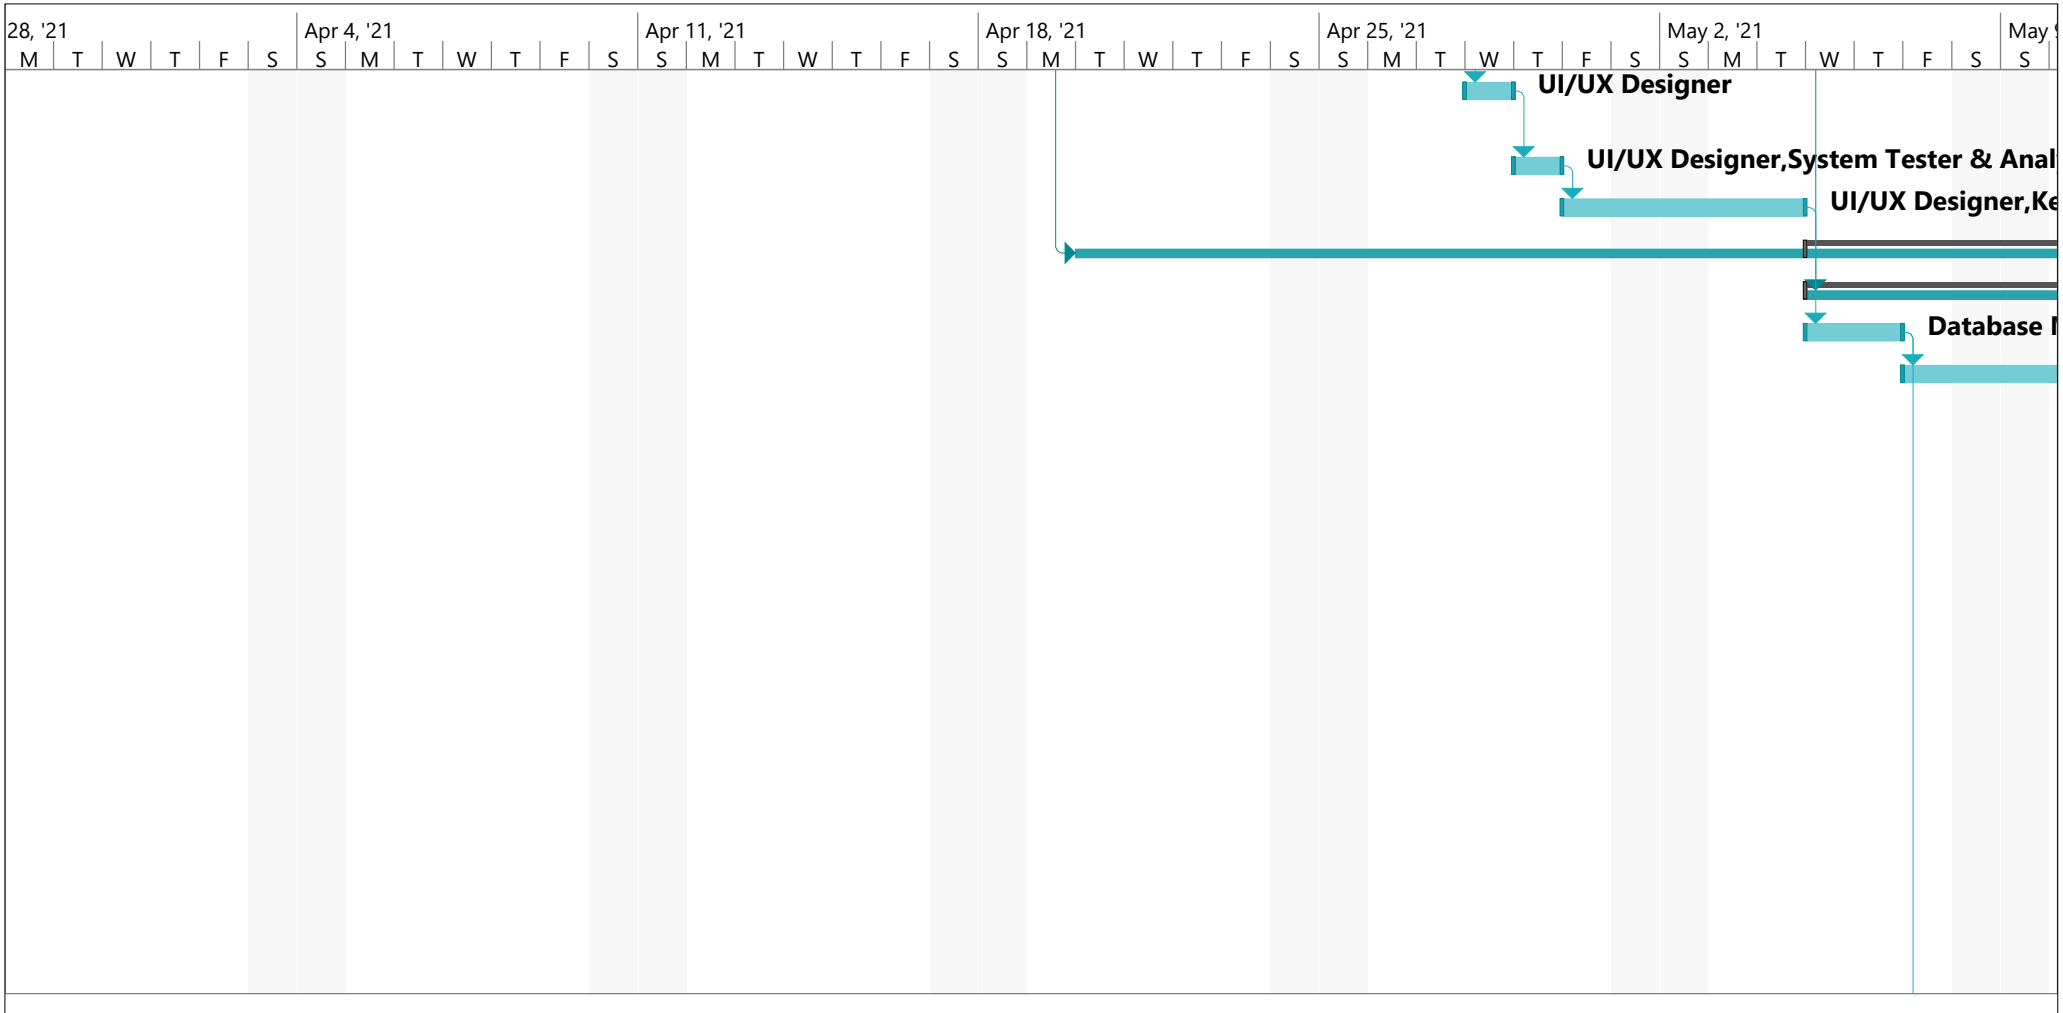

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

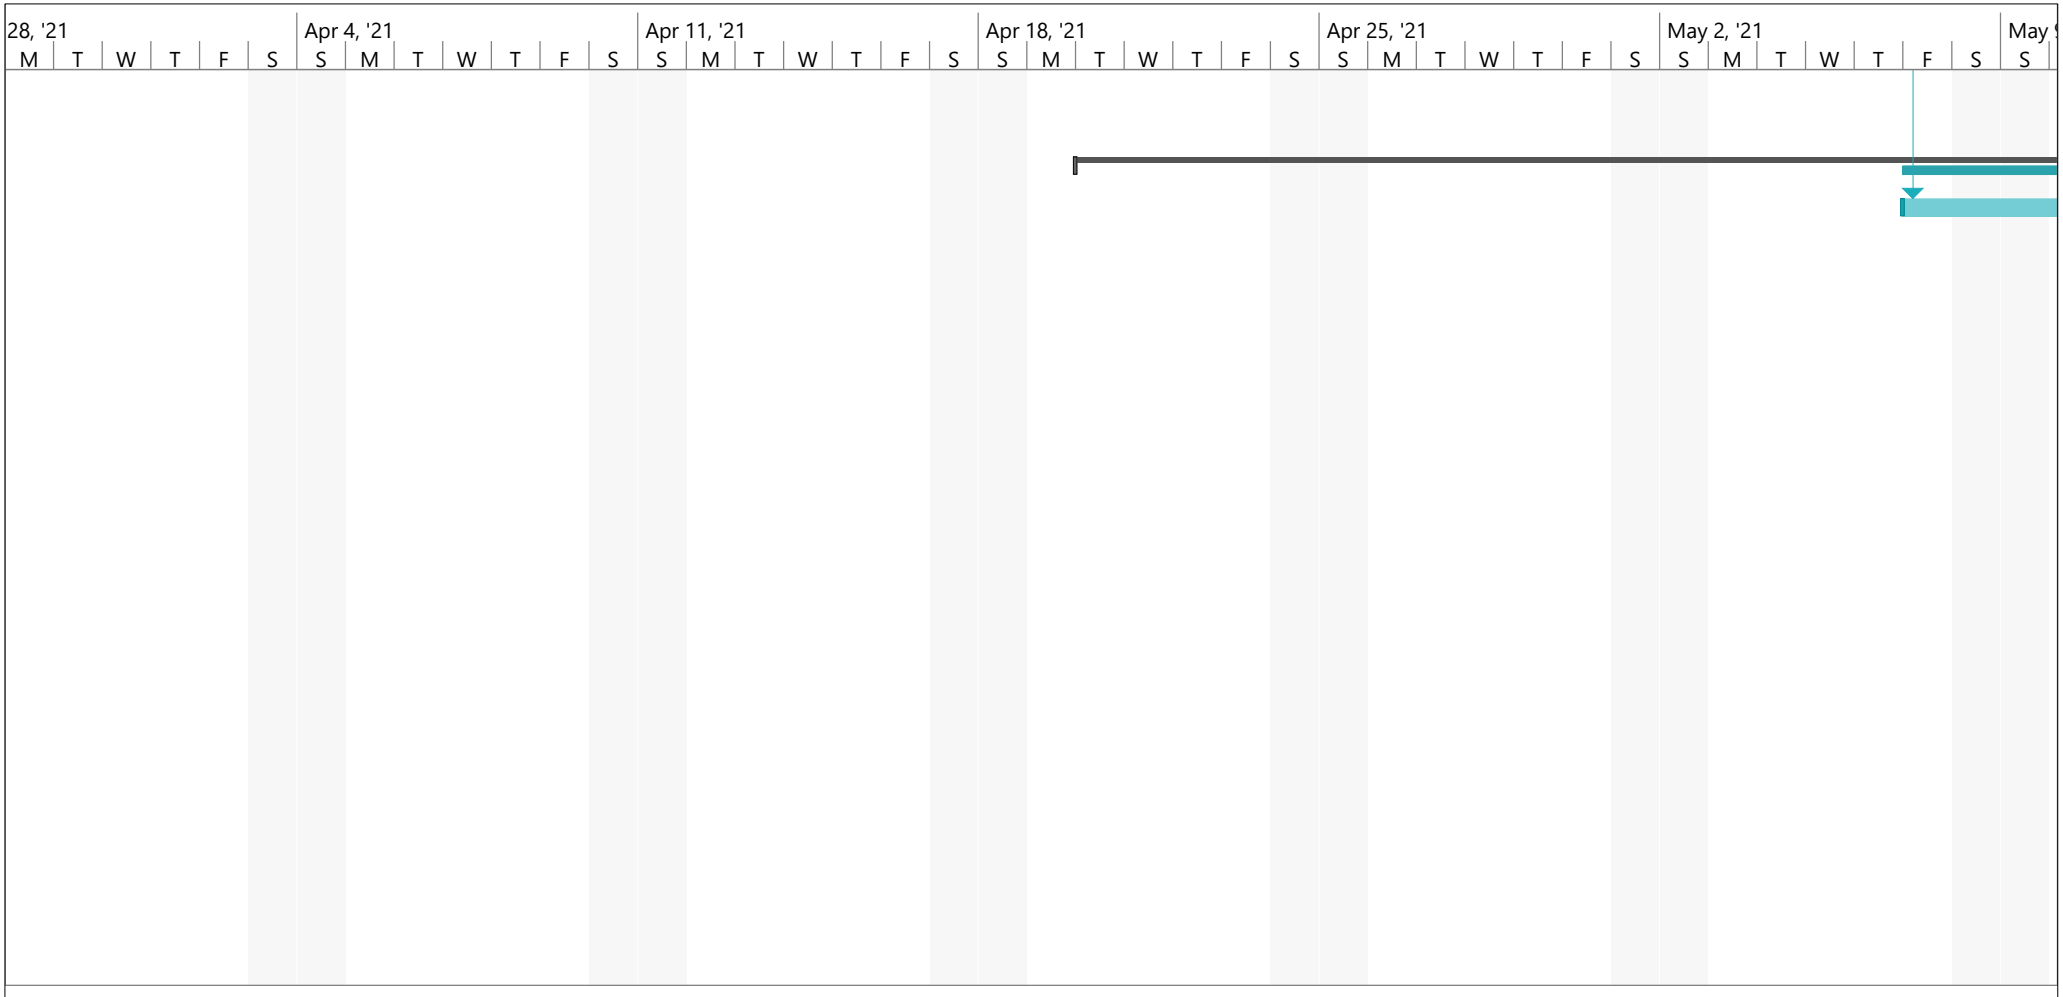

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	



Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

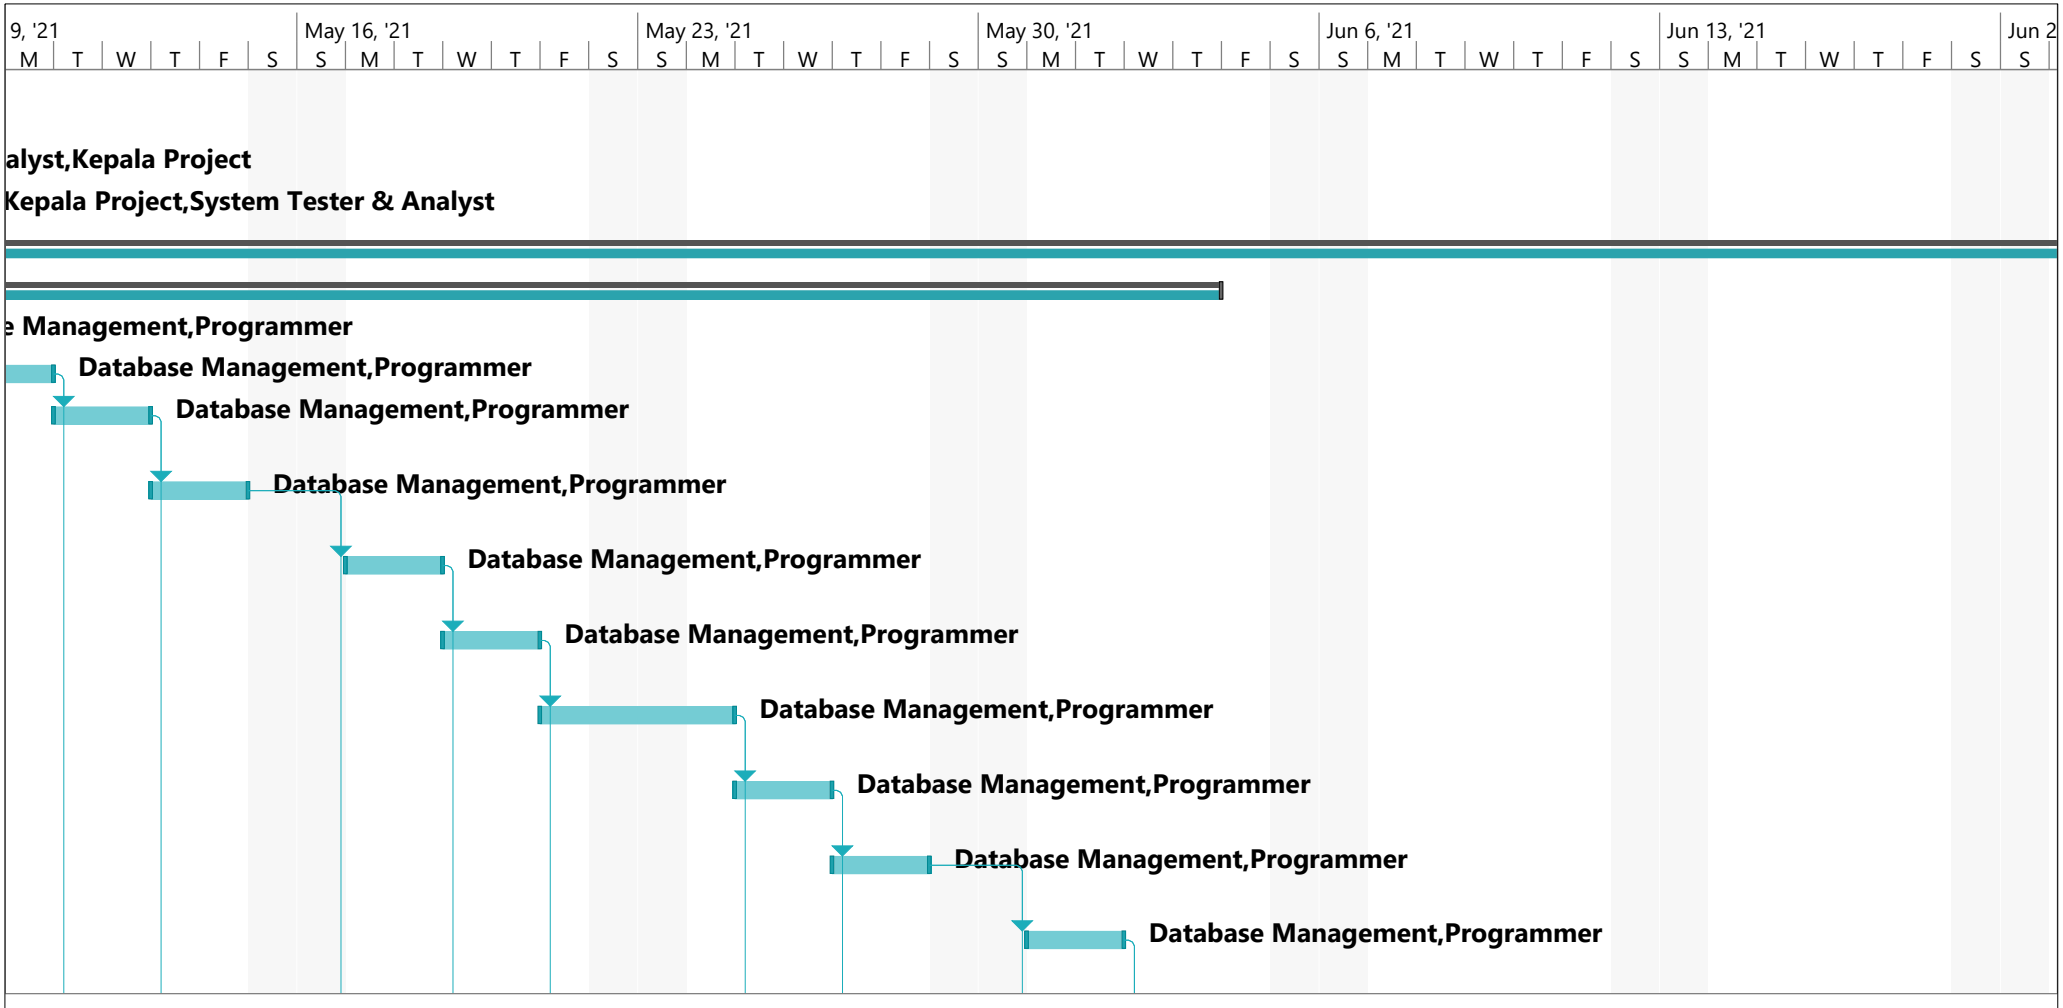

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

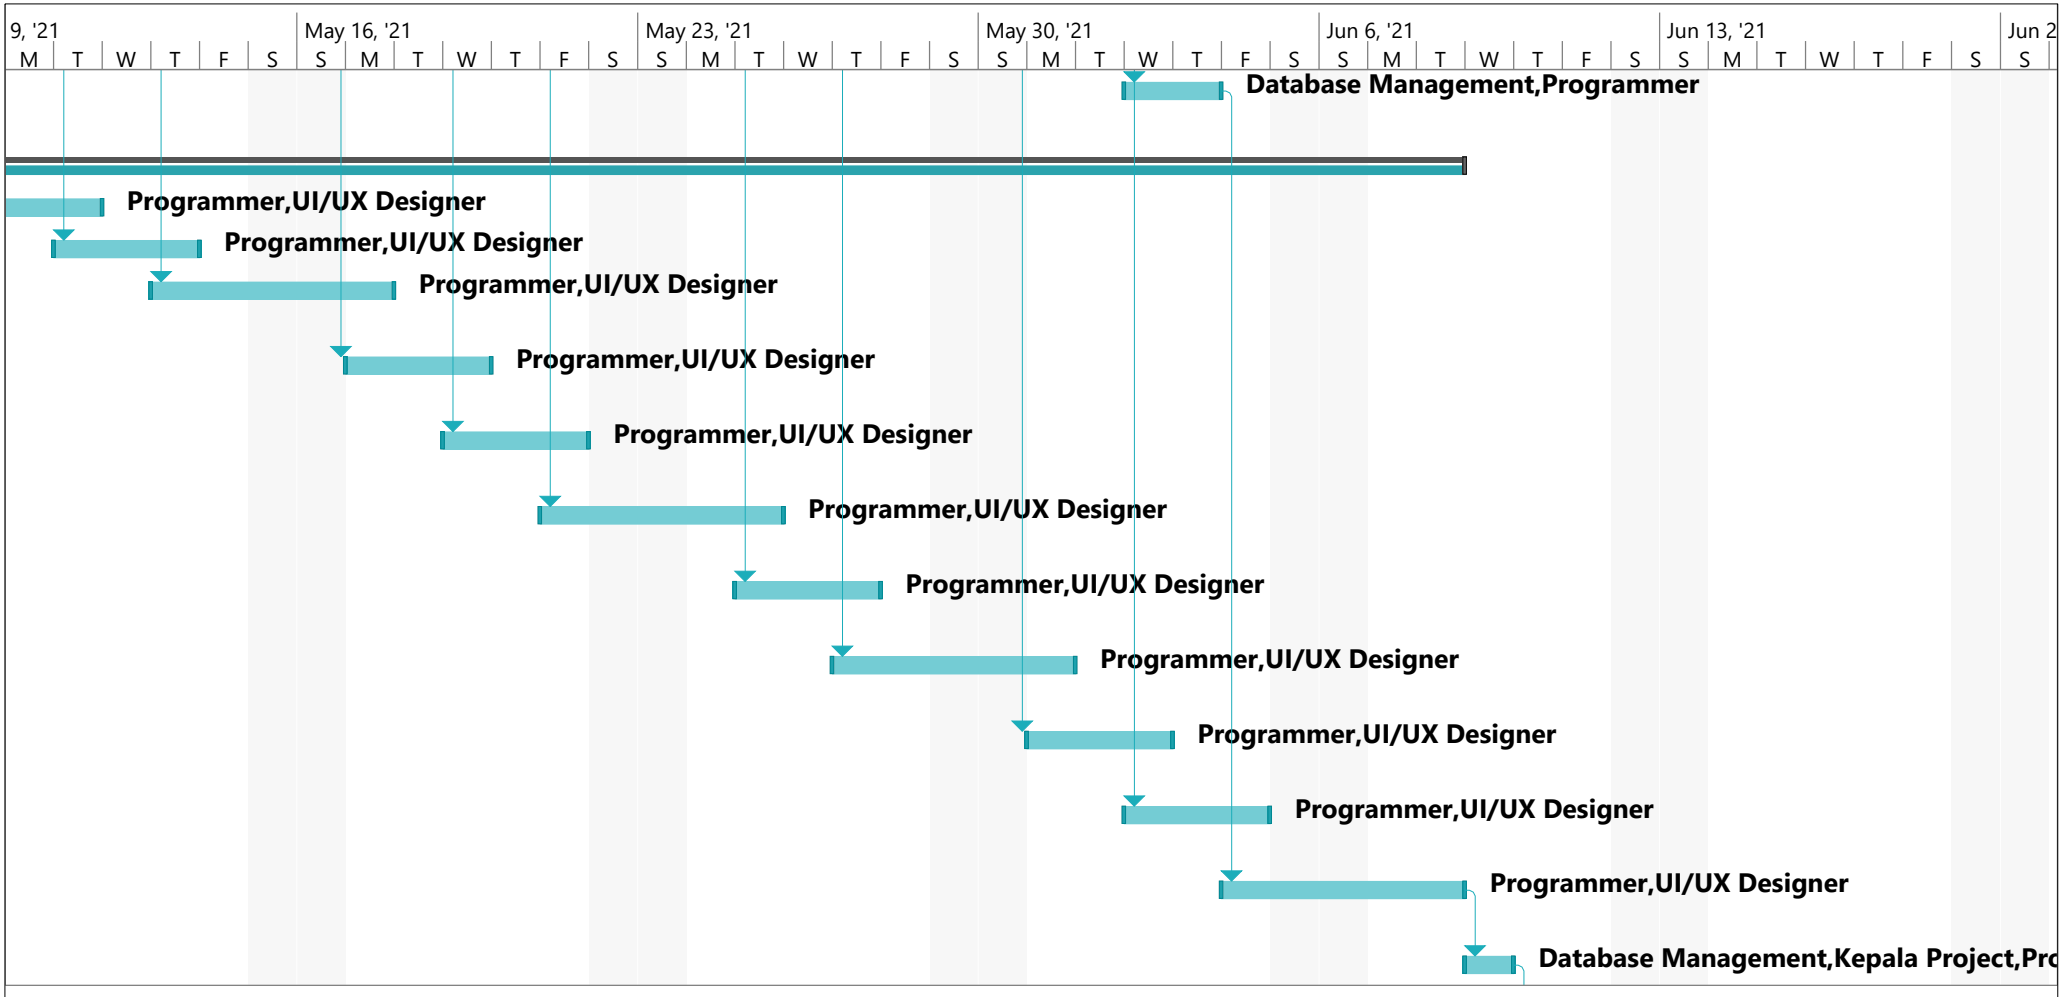

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

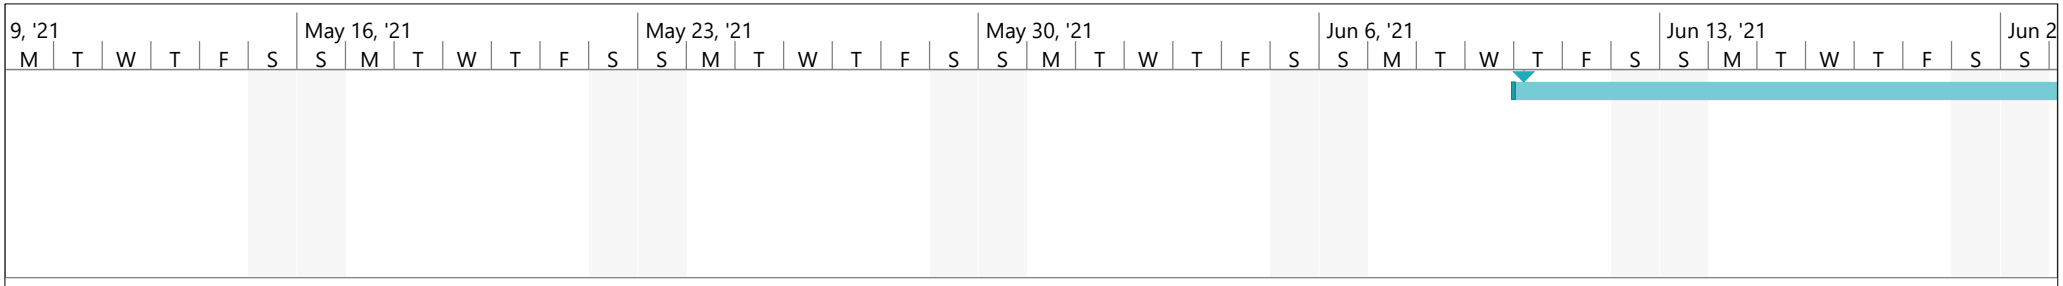

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

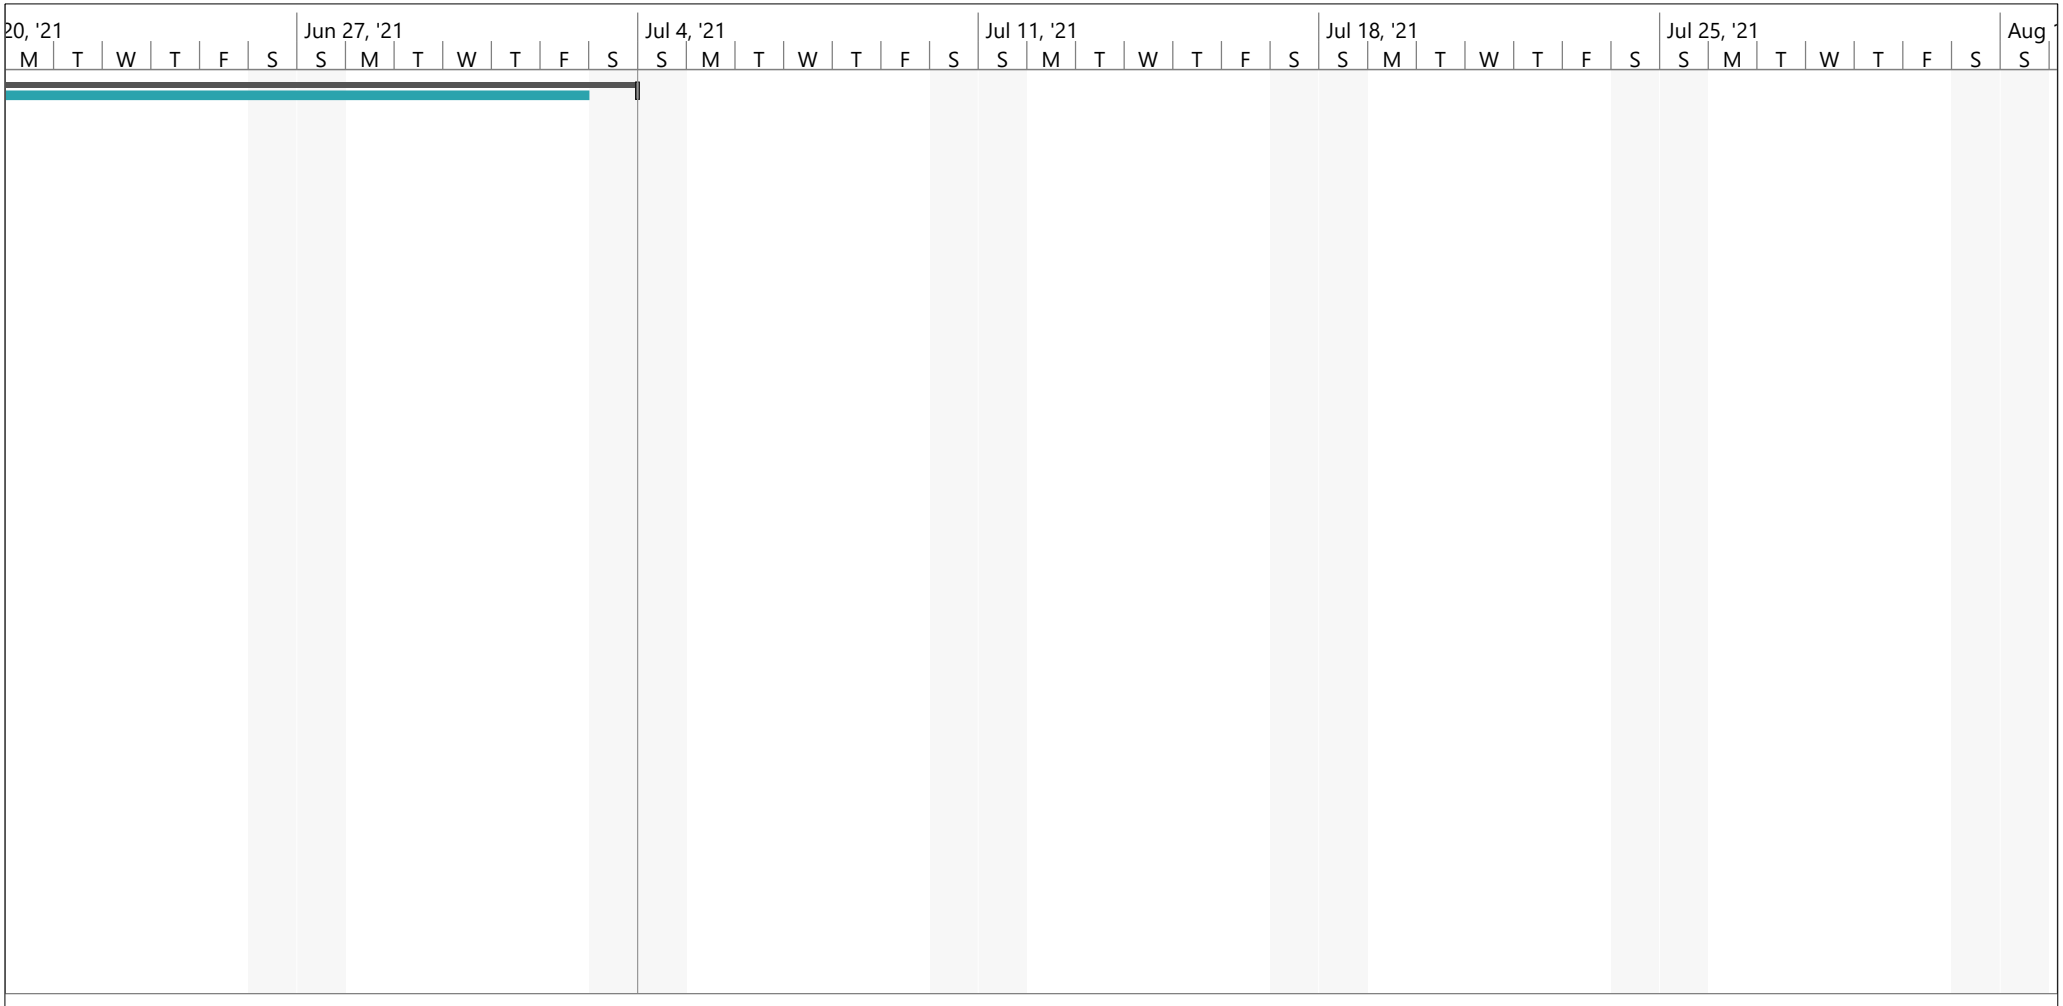

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

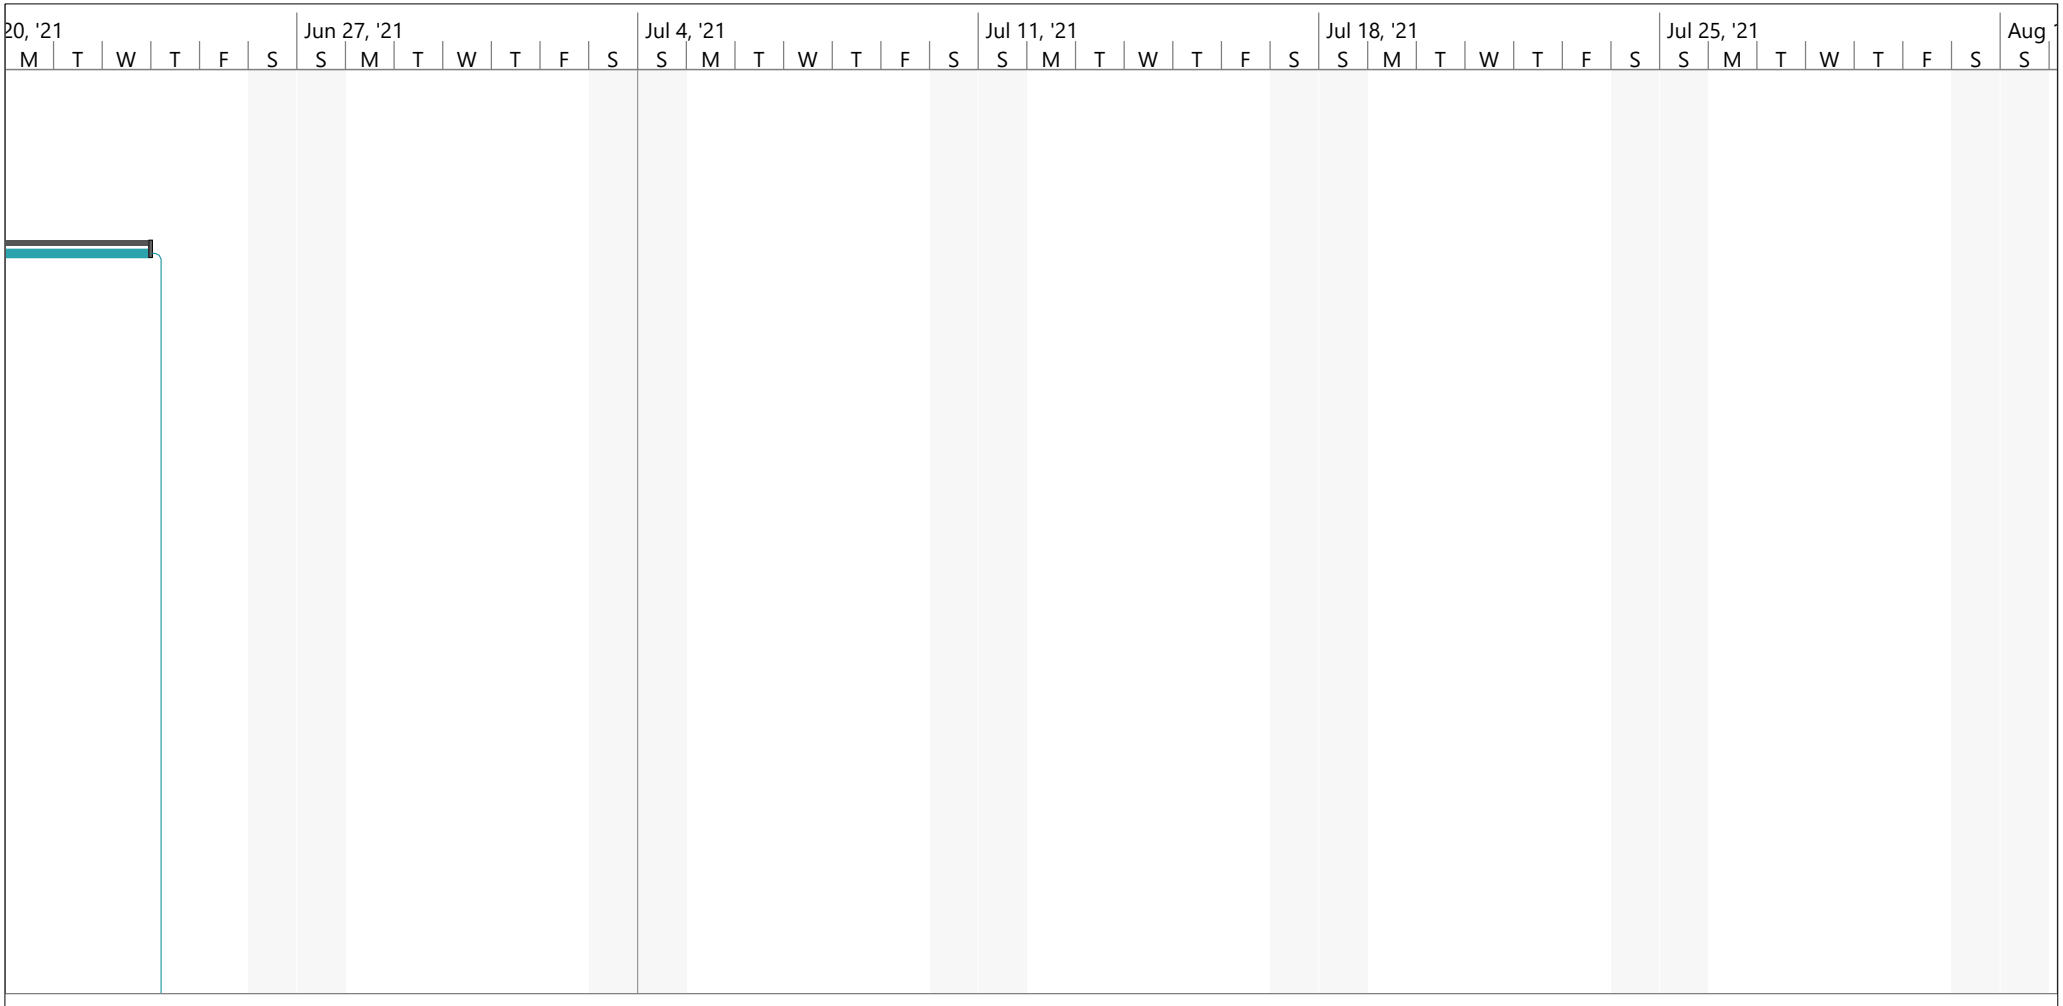

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

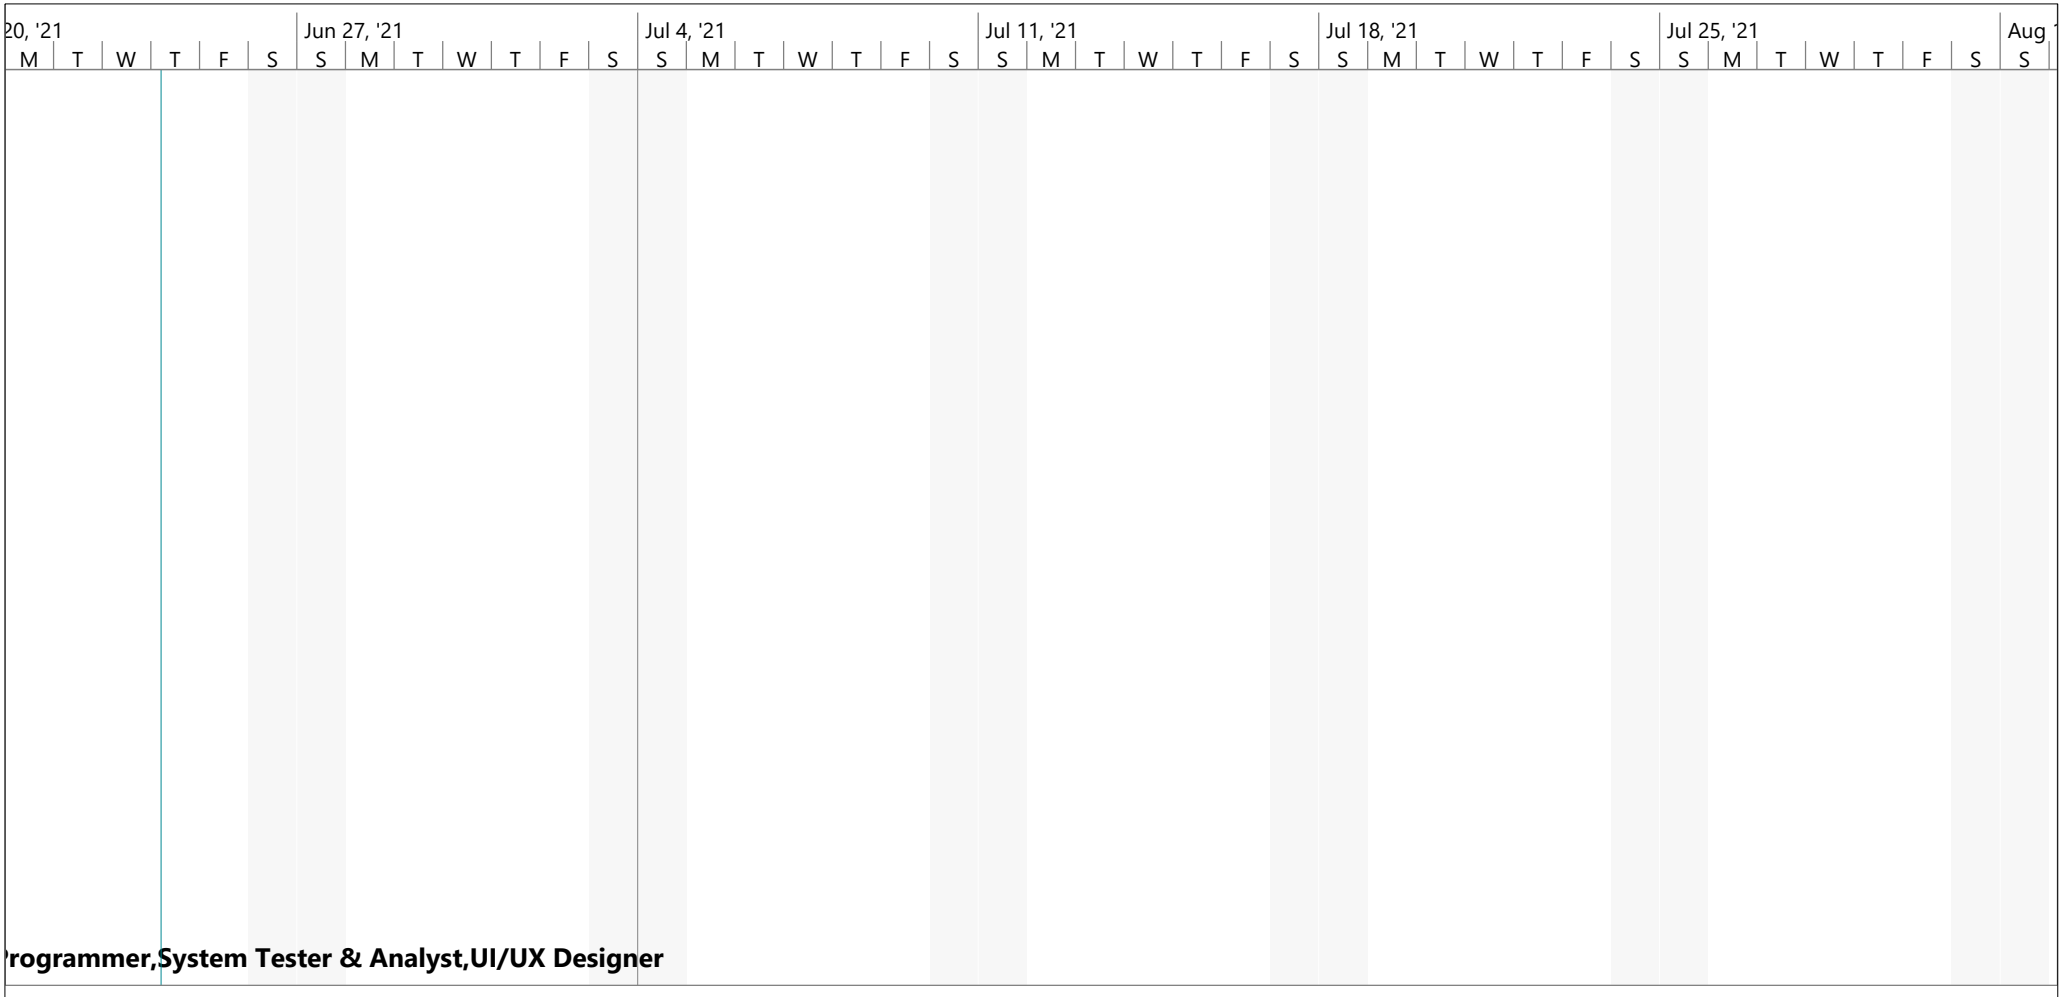

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

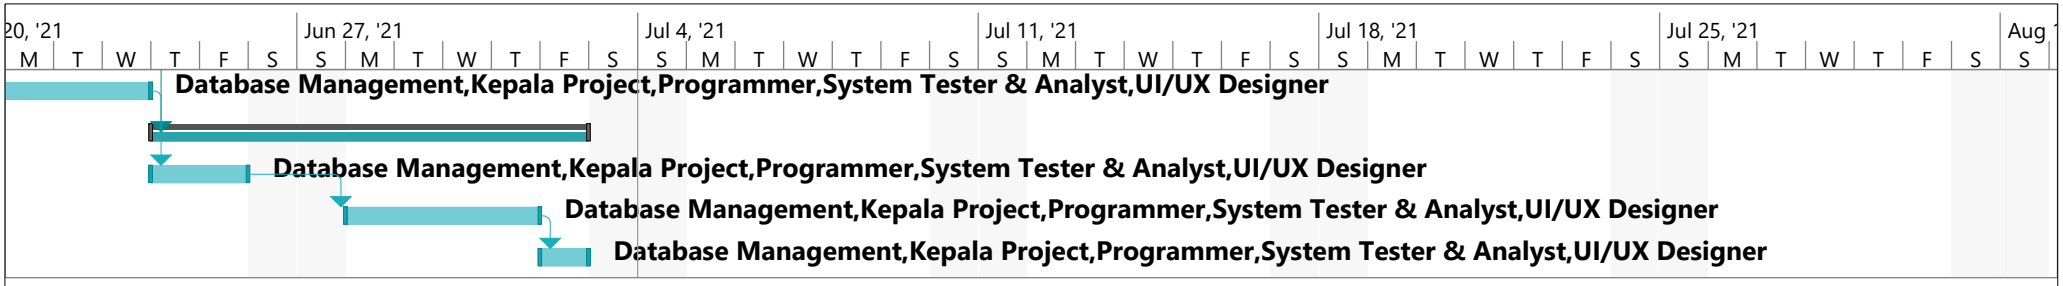

Project: PPL4611_KELOMPOK6_
Date: Wed 3/24/21

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
